


- ★ Fire Hydrant Locations
- ★ Fire Department Standpipe
- ★ Existing Egress Exit Locations
- Pedestrian Path
- Ambulance Path
- Hospital Delivery
- ED Walk-in Access
- Vehicle Path / Direction
- Construction Perimeter
- Work Zone
- Gates
- Parking
- LF Landry/French Field Office

May 19, 2025 - June 5, 2025

Site Demolition & Prep Scope:

- Building Removal
- Site wide Cleaning & Erosion Control

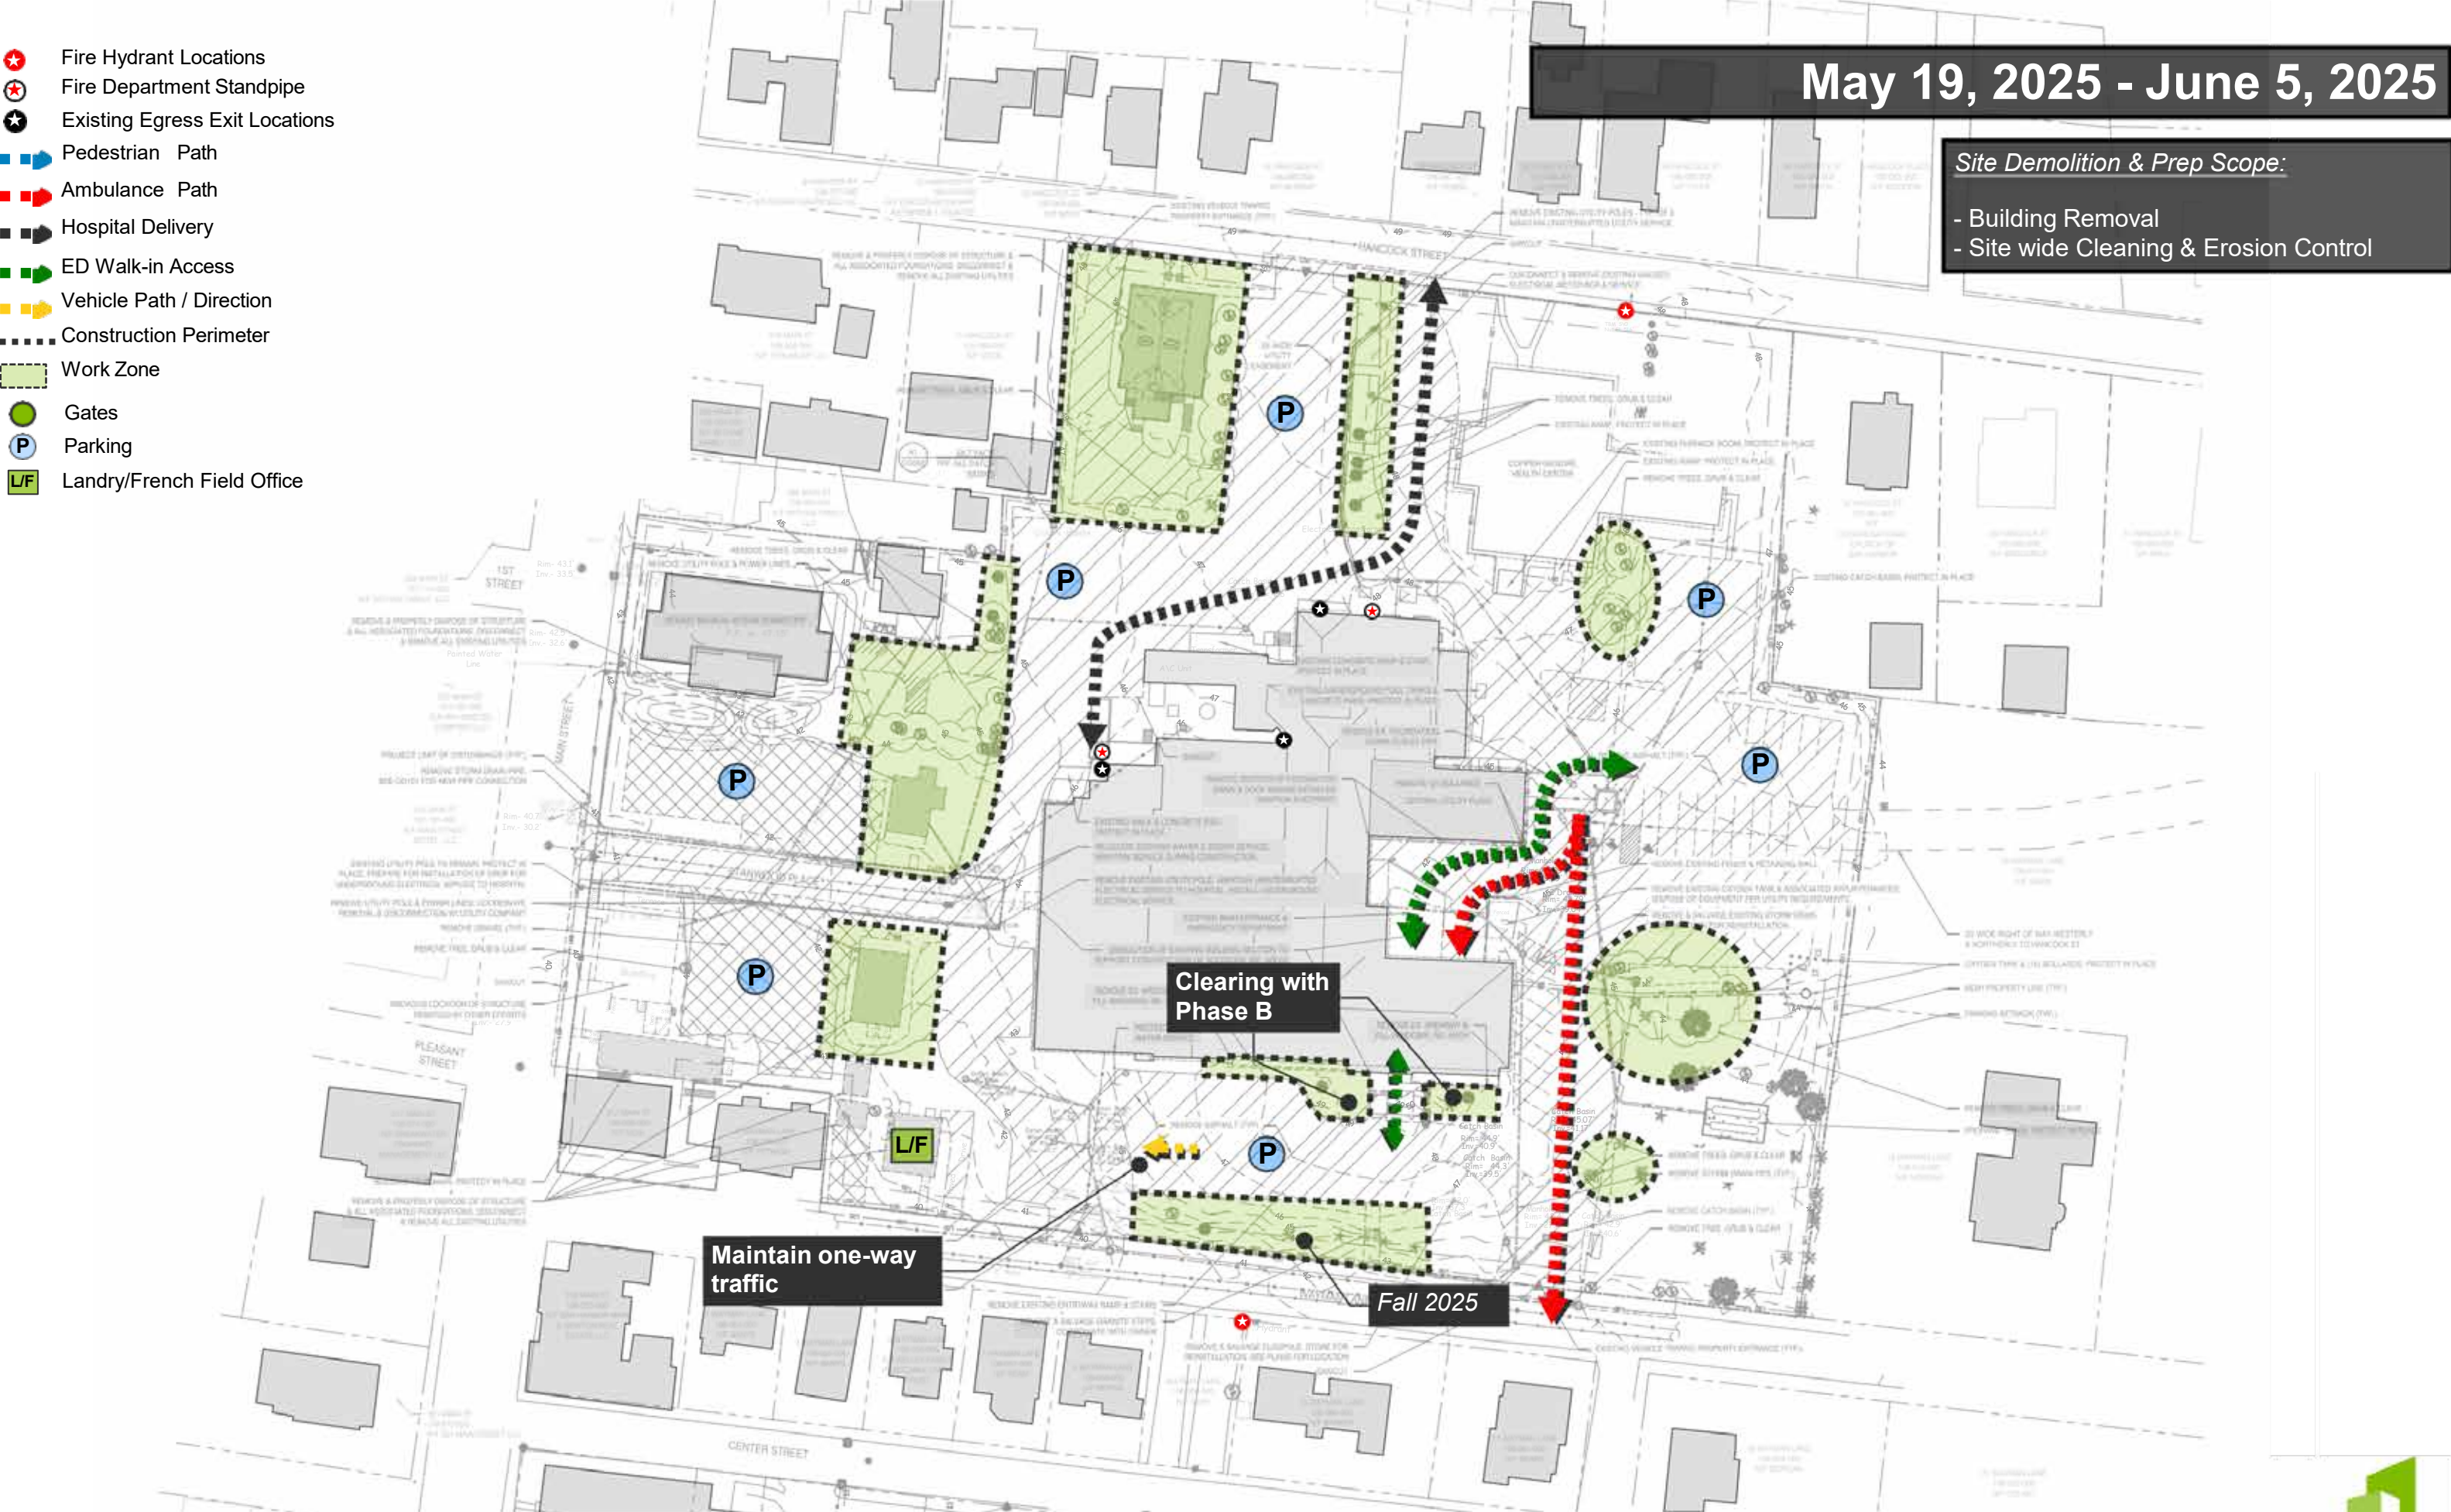


- ★ Fire Hydrant Locations
- ★ Fire Department Standpipe
- ★ Existing Egress Exit Locations
- Pedestrian Path
- Ambulance Path
- Hospital Delivery
- ED Walk-in Access
- Vehicle Path / Direction
- Construction Perimeter
- Work Zone
- Gates
- Parking
- LF Landry/French Field Office

June 11, 2025 - July 28, 2025

Hancock Temporary Parking Scope:

- Build Hancock temporary parking
- Build Hancock Exit connection

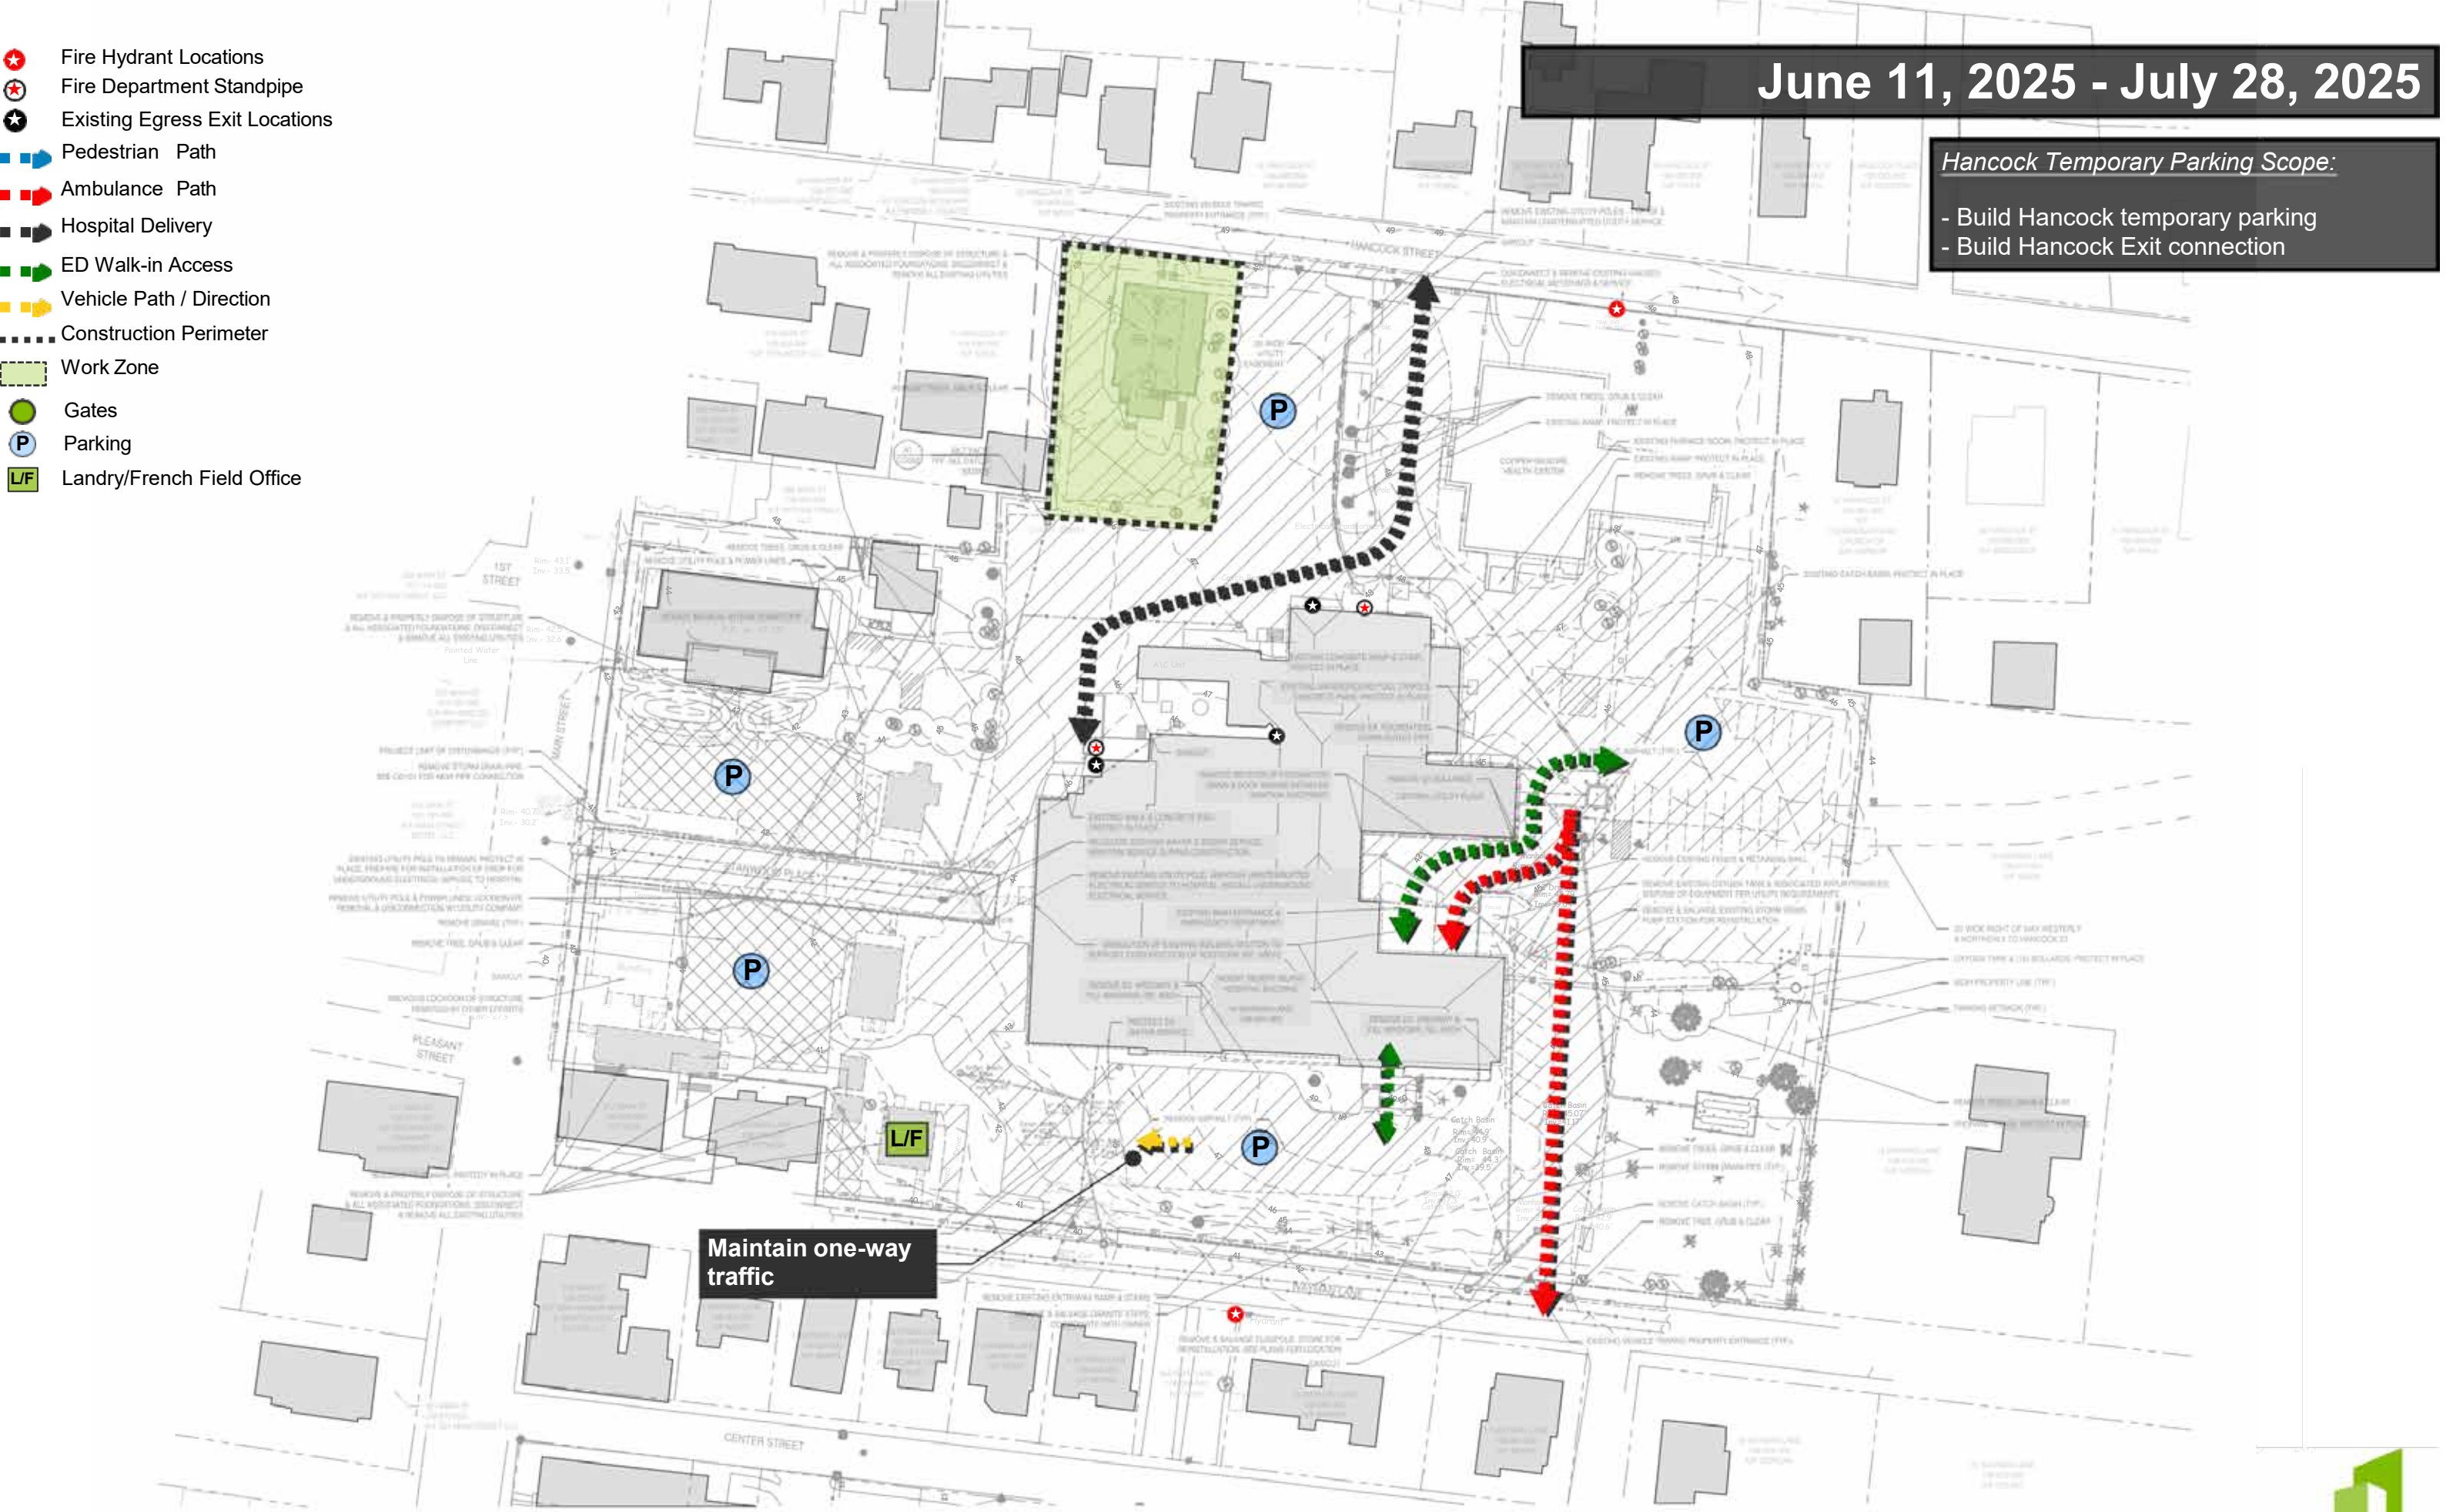

July 29, 2025 - August 20, 2025

West Side Drainage Scope:
- New drainage West / Main Street side
- Utility pole removal

- Fire Hydrant Locations
- Fire Department Standpipe
- Existing Egress Exit Locations
- Pedestrian Path
- Ambulance Path
- Hospital Delivery
- ED Walk-in Access
- Vehicle Path / Direction
- Construction Perimeter
- Work Zone
- Gates
- Parking
- Landry/French Field Office

Work Progress - East to West

Maintain one-way traffic



August 21, 2025 - September 2026

Phase C1 & C2 Scope:

- Construct new Main Entry Addition
- Construct new driveway & parking areas
- Demolition of 310 Main Street
- Construct Lab Renovations
- Executed concurrently w/ ED Enabling Phase (see separate plan)

- ★ Fire Hydrant Locations
- ★ Fire Department Standpipe
- ★ Existing Egress Exit Locations
- Pedestrian Path
- Ambulance Path
- Hospital Delivery
- ED Walk-in Access
- Vehicle Path / Direction
- Construction Perimeter
- Work Zone
- Gates
- Parking
- Landry/French Field Office

Barrier with fence & screen

Maintain Pedestrian Access

Primary site gate

Demo 310 Main Street
September, 2025

Alternate Pedestrian Path

Maintain one-way traffic

ED Enabling Phase
July 29, 2025 - December 30, 2025

Temp. Enabling Site Area S1-E1 Scope:

- Install new drainage
- Excavation / Hammering edge
- CB / Decon Tank / Piping
- Retaining wall / Foundation
- O2 Lines / Tank Installation & pad / bollard
- Backfill / Pave areas
- Temporary Canopy
- Temporary RTU

Maintain existing parking area

Maintain Pedestrian Access

New Main Entry Phase
August 21, 2025 - September 14, 2026

Maintain access at all times

Maintain Two Way Traffic

New Temp Entrance and Walk-In ER drop off

New Directional Signage

New ER Drop Off/Turn Around Area

Area closed as needed for tie-ins on Wayman Lane



January 2026 - July 2027

New directional signs added

ED Addition - Area A Scope:
- Construct New ED Addition, Canopy, and Site Improvements

Temporary parking lot entrance

New directional signs added

New Temporary Entrance

Maintain Two Way Traffic

New ER Drop Off/Turn Around Area

New Directional Signage

New Directional Sign - Ambulance Entrance Only

Maintain access at all times


Area kept clear from O2 delivery

- Fire Hydrant Locations
- Fire Department Standpipe
- Existing Egress Exit Locations
- Pedestrian Path
- Ambulance Path
- Hospital Delivery
- ED Walk-in Access
- Vehicle Path / Direction
- Construction Perimeter
- Work Zone
- Gates
- Parking
- Landry/French Field Office

Construct Final Site Improvements in Coordinated Phases (North Lot, South Entry, and then West Green Space

ED Walk-in Addition - Area B Scope:

- Construct New ED Walk-In Addition
- Construct ED Renovation
- Complete Final Site Improvements in Phases

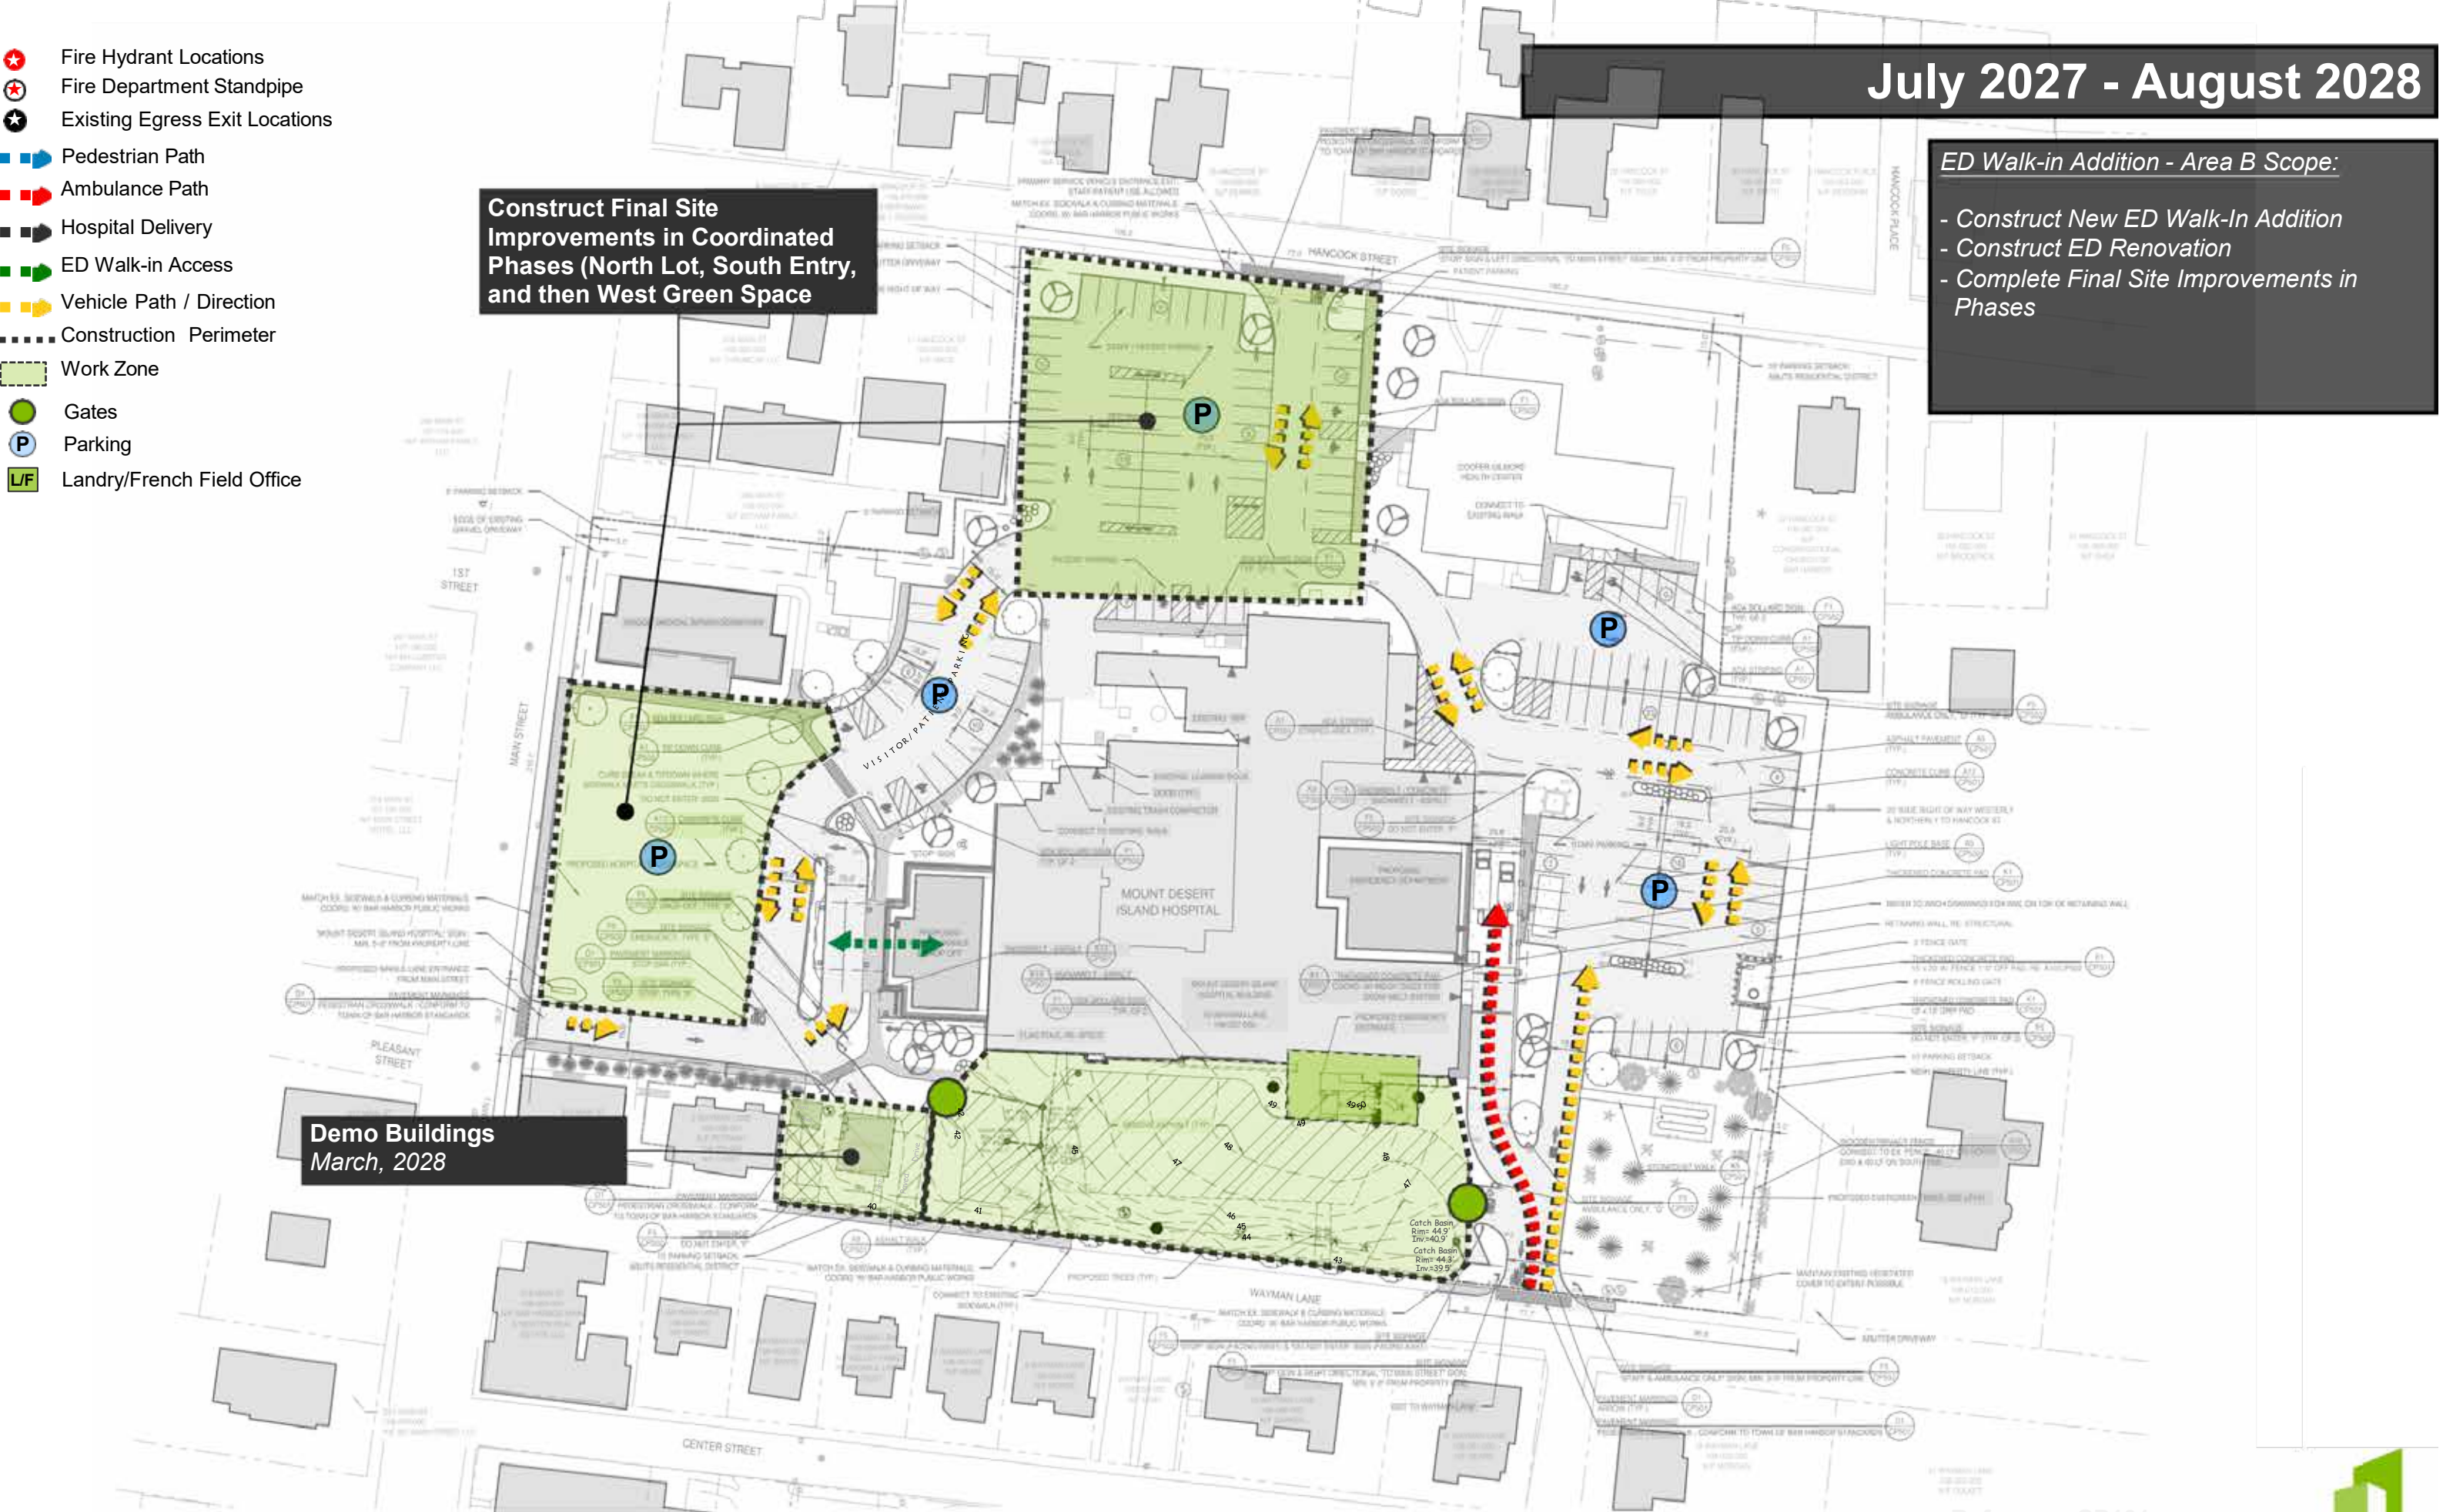

Demo Buildings
March, 2028

